



Monthly Measure J Bond Program Status Report July 31, 2011

I. EXECUTIVE SUMMARY

The District continues to study what project re-prioritizing is necessary with any remaining balance of Series C funds of Measure J Bond projects not already in construction. The scope of work and budget for projects currently in design will be impacted as a result of the action the Board has taken on moving forward with the Clear Lake Campus and Sutter County Campus projects.

Construction at Woodland Community College, the renovation of Buildings 100, 200 (exterior painting only), 300 and 400 is nearly complete. Work on all four buildings is planned for completion prior to the start of the 2011 Fall Semester.

At Yuba College, construction continues on the renovation of the gymnasium (Building 1200). Most work has been completed on the east side of the building, and the contractor's attention is now focused on the gym itself and the west locker rooms. Construction is scheduled for completion by the end of August 2011.

Also at Yuba College, the Health and Public Safety Building is nearing completion with final mechanical and electrical work being completed along with interior touch-ups. All this is in preparation for the installation of Furniture, Fixtures and Equipment and move in of staff and faculty prior to the start of the Fall Semester.

Construction has also begun on the Educational Building at the Sutter County Campus with the building site pad work, including foundation work, moving ahead.

Swing Space and Move-out planning for Building 1100 continue as meetings are scheduled to confirm space and infrastructure needs of each department and program being temporarily relocated. The logistics of the moves themselves, as well as all of the other logistical challenges posed by such a complex effort, continue to be reviewed to ensure a smooth transition to temporary facilities. Modifications to spaces within Building 300 and 1700 and the move-out of Library and Media Services functions from Building 1100 have gone smoothly. Other functions still remaining in Building 1100 will be moved during the months leading up to December 2011. Start of construction of this State-funded project is scheduled for January 2012.

II. MASTER SCHEDULE SUMMARY

The Measure J Bond Program Master Schedule is updated with current status on a monthly basis in order to track the progress of design consultants and contractors against the baseline Implementation Plan.

A six month look-ahead schedule (containing only those activities occurring within the six months of the program following the date of the reporting period) is included as Attachment A to this report. For the full and summary schedules, see the Quarterly Report dated March 31, 2011.

III. COST REPORT

The current Program Cost Summary (Attachment B) was created using the District Cost Report dated July 31, 2011.

IV. FUNCTIONAL AREA REPORTS

Refer to the latest Quarterly Report dated March 31, 2011, for Program Controls, Contracts, Solicitation and AECOM CM Project Amendments as well as Planning/Pre-Design updates.

V. PROJECT STATUS (Attachment C)

Design Activities Summary

Yuba College – Marysville

J-07 – Building 500, Business Department – (DLR Architects)

- DSA approval has been obtained. Further progress on this project will be dependent on District determination of available funding.

J-09 – Building 700, Math/Engineering/Computer – (DLR Architects)

- DSA approval has been obtained. Further progress on this project will be dependent on District determination of available funding.

J-16 – Building 1300 – Collins Hall (ImageWorks)

- Work on this building has been deferred pending re-evaluation by the college of future plans for the building.

- J-19 – Building 1600 – Warren Hall (ImageWorks)
- Work on this building has been delayed pending re-evaluation by the college of future plans for the building, including swing space use.

Campus Quad, Multi-Building Renovations (LPAS)

J-02 – Building 100A, Administration Building

J-03 – Building 100B, Student/Instruction Services

J-04 – Building 200, Music Department

- Schematic Design - further development of the design will depend on possible reallocation of available Series C Bond funds.

J-05 – Building 300, Student Center / Bookstore

- Design Development - further development of the design will depend on possible reallocation of available Series C Bond funds.

J-13 – Building 1100, Library & Language Arts – State Funded

- State Chancellor's Office has authorized the open public bidding of the project. The project will no longer be constructed as a Lease/Leaseback project.
- Move-out planning meetings continue to be scheduled to prepare for the start of construction in January 2012. Modifications to temporary relocation spaces in Buildings 300 and 1700 have been completed.
- Library and Media Services moves to Building 300 and 1700 have been successfully completed and are operational for the start of fall semester.

Yuba College – Clear Lake Campus

J-32 – Student Services Building

- Increment 2 Building – Comments have been received from DSA and are currently being addressed by the architect. The back-check meeting with DSA has been scheduled for August 24, 2011.

District

J-01 – Sutter County Facility, District Component (tBP Architects)

- District Office Building – Further progress on this project will be dependent on District determination of available funding.

Construction Activities Summary

Woodland Community College

J-42 – Colusa County Outreach Facility

- The building is open for school while Hilbers Inc. of Yuba City is working on outstanding punch list items in and around the building.
- Landscaping is now 95% complete.
- Site work is approximately 85% complete.

J-39 – Bldgs. 100/300/400 Reroof – Increment 1

- Work has been completed on the Reroofing Increment of this project.
- The architect has accepted the project as complete.

J-39 – Bldgs. 100/300/400 Renovations – Increment 2

- Phase 1A – is remodeling Bldg 100, Phase 1B is upgrading hydronic piping systems for Bldgs 100/300/400; and Phase 2 is the remodeling the inside Bldgs 300 & 400.
- Phase 1A work is complete except for multiple punchlist items and a few finishing touches.
- Phase 1B – Hydronic piping is complete from the new chiller to Bldg 100 and to Bldg 300/400. All excavation work is complete and backfilled and landscape repairs are planted
- Phase 2 work has begun May 25th and well under way. Walls are framed, sheetrocked and painted, flooring is going down and electrical & plumbing work is in the finish phase.

Yuba College – Marysville

J-14 – PE Complex Modernization – Vol. I Athletic Fields

- Final punch list and closeout remains to be performed.

J-14 – PE Complex Modernization – Vol. II Building Renovation

- Office and classroom areas are complete with furniture installed.
- New Mat Room will be complete for the start of school semester.
- Gymnasium floor and bleachers will be complete mid-September.
- West side locker room renovation will be complete mid-September.
- Women's Team Rooms completion has been delayed.

J-25 – Health & Public Safety Building (Increment II)

- Building is complete and in punchlist corrections
- Furniture is been installed and faculty move-in next month
- Exterior hardscape/landscape continues to be installed

Yuba College - Sutter County Campus

J-01 – Sutter County Facility

- Educational Building (Increment 2) – Construction has begun with initial building foundation work proceeding.

Yuba College – Clear Lake Campus

J-32 – Student Services Building

- Increment 1 Site Work – Construction started late May following end of classes and scheduled for completion prior to the start of fall semester.

J-33 – Renovation of Portables & Utilities Upgrade

- No activity to report.

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish	2010 2011 2012																											
						2010			2011												2012												
						O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	A
Woodland Community College Campus																																	
J-39 Multi Bldg Renovations - Bldgs 100 - 400																																	
WCJ394110	Advertise/Solicit for Bid	5	0	07JAN11A	14JAN11A	■ Advertise/Solicit for Bid																											
WCJ394115	Bid Period	22*	0*	07JAN11A	07FEB11A	■ Bid Period																											
WCJ394120	Pre Bid Conference & Site Visit	0	0	27JAN11A		◆ Pre Bid Conference & Site Visit																											
WCJ394125	Bid Opening	0	0	08FEB11A		◆ Bid Opening																											
WCJ394130	Bid Evaluation	5	0	08FEB11A	14FEB11A	■ Bid Evaluation																											
WCJ394135	Contractor's Bid Protest Period	5	0	08FEB11A	14FEB11A	■ Contractor's Bid Protest Period																											
WCJ394140	Prepare Board Notice of Intent to Award	5	0	08FEB11A	14FEB11A	■ Prepare Board Notice of Intent to Award																											
WCJ395100	District Issues Construction Contract	10	0	15FEB11A	28MAR11A	■ District Issues Construction Contract																											
WCJ394145	Board of Trustees Approval of Contract Award	0	0	16FEB11A		◆ Board of Trustees Approval of Contract Award																											
WCJ395110	Submit Bonds, Licenses & Insurance	5	0	22FEB11A	28FEB11A	■ Submit Bonds, Licenses & Insurance																											
WCJ395120	Pre-Construction Meeting	0	0	08MAR11A		◆ Pre-Construction Meeting																											
WCJ395140	Bldg 100 Renovation - Phase 1	91	14	14MAR11A	18AUG11	■ Bldg 100 Renovation - Phase 1																											
WCJ395130	Issue NTP	0	0	21MAR11A		◆ Issue NTP																											
WCJ395170	Bldg 100 Chiller Installation w/ U/G Piping	36*	0*	01JUN11A	21JUL11A	■ Bldg 100 Chiller Installation w/ U/G Piping																											
WCJ395150	Bldgs 300 & 400 Renovation Constr - Phase II	62*	16*	25MAY11A	22AUG11	■ Bldgs 300 & 400 Renovation Constr - Phase II																											
J-34 Performing/Culinary Arts - ON HOLD																																	
WCJ341100	A/E Selection Process	15	0	04JAN11A	24FEB11A	■ A/E Selection Process																											
WCJ341110	PROJECT START DATE TO BE DETERMINED	0	0	01AUG11*		◆ PROJECT START DATE TO BE DETERMINED																											
J-36 Multi-Purpose Athletic Bldg - ON HOLD																																	
WCJ361000	PROJECT START DATE TO BE DETERMINED	0	0	01AUG11		◆ PROJECT START DATE TO BE DETERMINED																											
J-42 New Bldg - Colusa Co. Out-Reach Facility																																	
CCJ427100	PMT & A/E Develop Punch List	15	0	11JAN11A	31JAN11A	■ PMT & A/E Develop Punch List																											
CCJ427110	Systems Start-Up	5	0	25JAN11A	31JAN11A	■ Systems Start-Up																											
CCJ427120	Punch List Corrections	103*	20*	04APR11A	26AUG11	■ Punch List Corrections																											
CCJ427130	As-Built Drawings	10	0	04APR11A	08APR11A	■ As-Built Drawings																											
CCJ427150	Manuals & Warranty	5	0	04APR11A	08APR11A	■ Manuals & Warranty																											
CCJ427140	Systems Training	10	0	11APR11A	15APR11A	■ Systems Training																											
CCJ427160	Issue Certificate of Completion Of Construction	0	0		02SEP11	◆ Issue Certificate of Completion Of Construction																											
CCJ427170	Beneficial Occupancy	0	0		02SEP11	◆ Beneficial Occupancy																											
CCJ427180	Release Retention to Contractor	0	0		26SEP11	◆ Release Retention to Contractor																											

YCCD MEASURE J BOND PROGRAM

STATUS THROUGH JULY 31, 2011

MASTER SCHEDULE - SIX MONTH LOOKAHEAD

ATTACHMENT A

Subject to Revisions by Measure J Bond Requirements

**YUBA COMMUNITY COLLEGE DISTRICT
MEASURE J BOND PROGRAM
PROGRAM COST SUMMARY**

Totals as of July 31, 2011

		Current Project Budget	Total Estimated Construction Costs	Obligations / Commitments to Date	Paid to Date	Open Encumbrance	% Obligated	% Complete
Project	Other Bond Costs							
-	Issuance, Underwriting and Insurance Costs	\$ -	\$ -	\$ 1,713,582	\$ 1,713,582	\$ -	Complete	
Project	District Facilities/Systems							
J-01	Sutter County Facility	\$ 37,006,855	\$ 26,700,000	\$ 11,846,795	\$ 9,586,682	\$ 2,260,113	32.01%	25.91%
J-29	Payoff 11/05 Borrowing	\$ 4,971,026	\$ -	\$ 4,971,027	\$ 4,971,027	\$ -	Complete	
J-30	Technology/Telecoms/Security Sys	\$ 5,500,000	\$ 500,000	\$ 3,653,551	\$ 2,816,141	\$ 837,410	66.43%	51.20%
J-44	Bond Staff Support Costs	\$ -	\$ -	\$ 234,537	\$ 234,537	\$ -	See Footnote 1	
J-45	Clearing Account	\$ -	\$ -	\$ 731,932	\$ 376,629	\$ 355,302	See Footnote 1	
	Subtotal Allocated Costs	\$ 47,477,881	\$ 27,200,000	\$ 21,437,842	\$ 17,985,016	\$ 3,452,825	45.15%	37.88%
Project	Yuba College - Marysville							
J-02	Bldg 100A – Administration Bldg	\$ 732,693	\$ 500,340	\$ 133,326	\$ 52,934	\$ 80,392	18.20%	7.22%
J-03	Bldg 100B – Student/Instruction Services	\$ 3,579,961	\$ 2,589,940	\$ 413,671	\$ 181,753	\$ 231,919	11.56%	5.08%
J-04	Bldg 200 – Music Department	\$ 988,012	\$ 648,900	\$ 202,645	\$ 81,690	\$ 120,955	20.51%	8.27%
J-05	Bldg 300 – Student Center/Bookstore	\$ 4,554,149	\$ 3,500,000	\$ 641,336	\$ 294,190	\$ 347,146	14.08%	6.46%
J-06	Bldg 400 – Theatre	\$ 3,945,224	\$ 2,632,565	\$ 3,999,323	\$ 3,649,826	\$ 349,497	101.37%	92.51%
J-07	Bldg 500 – Business Dept (Classrooms)	\$ 3,563,155	\$ 2,000,000	\$ 753,694	\$ 548,874	\$ 204,820	21.15%	15.40%
J-08	Bldg 600 – Applied Arts, Science/Tech	\$ 743,247	\$ 502,963	\$ 699,607	\$ 696,018	\$ 3,589	94.13%	93.65%
J-09	Bldg 700 – Math/Engineering/Computer	\$ 2,181,821	\$ 1,531,654	\$ 379,597	\$ 270,665	\$ 108,931	17.40%	12.41%
J-10	Bldg 800 – Life Sciences & Nursing	\$ 166,654	\$ 112,722	\$ 163,526	\$ 162,676	\$ 850	98.12%	97.61%
J-11	Bldg 900 – Utilities Services	\$ 3,144,401	\$ 1,712,303	\$ 2,910,989	\$ 2,877,161	\$ 33,828	92.58%	91.50%
J-12	Bldg 1000 – Liberal Arts Consumer Ed	\$ 1,671,909	\$ 925,944	\$ 1,492,252	\$ 1,489,730	\$ 2,522	89.25%	89.10%
J-13	Bldg 1100 – Library & Language Arts	\$ 23,360,562	\$ 16,536,000	\$ 2,044,884	\$ 1,184,960	\$ 859,924	8.75%	5.07%
J-14	Bldg 1200 – PE Complex	\$ 12,952,157	\$ 9,948,515	\$ 13,252,496	\$ 10,355,439	\$ 2,897,057	102.32%	79.95%
J-15	Bldg 1250 – ESL (Demolish Structure)	\$ 124,793	\$ 100,000	\$ 5,322	\$ 5,322	\$ -	4.26%	4.26%
J-16	Bldg 1300 – Collins Hall – Staff Offices	\$ 45,523	\$ 2,805	\$ 36,991	\$ 36,991	\$ -	81.26%	81.26%
J-17	Bldg 1400 – Maintenance/Print Shop	\$ 1,238,017	\$ 884,822	\$ 42,442	\$ 42,442	\$ -	3.43%	3.43%
J-18	Bldg 1500 – Osuna (Decommission)	\$ 440,162	\$ 348,763	\$ 9,398	\$ 9,398	\$ -	2.14%	2.14%
J-19	Bldg 1600 – Warren Hall	\$ 383,657	\$ 300,241	\$ 54,747	\$ 54,747	\$ -	14.27%	14.27%
J-20	Bldg 1700 – Automotive	\$ 109,869	\$ 75,873	\$ 16,708	\$ 16,708	\$ -	15.21%	15.21%
J-21	Bldg 1800 – Student Services DSPS	\$ 558,389	\$ 382,839	\$ 570,488	\$ 569,950	\$ 538	102.17%	102.07%
J-22	Bldg 1900 – Distributive Ed Center	\$ 67,443	\$ 14,050	\$ 72,459	\$ 71,207	\$ 1,252	Complete	
J-23	East Parking Lot (included in J-25)	\$ -	\$ -	\$ -	\$ -	\$ -	-	-
J-24	New Soccer Field (included in J-14)	\$ -	\$ -	\$ -	\$ -	\$ -	-	-
J-25	Allied Health & Public Safety Building	\$ 20,590,979	\$ 17,150,814	\$ 23,164,771	\$ 17,511,776	\$ 5,797,389	112.50%	85.05%
J-26	Upgrade Press Box/Score Board, Etc. (Included in J-14)	\$ -	\$ -	\$ -	\$ -	\$ -	-	-
J-27	Demolition Pool (Included in J-14)	\$ -	\$ -	\$ -	\$ -	\$ -	-	-

Attachment B

**YUBA COMMUNITY COLLEGE DISTRICT
MEASURE J BOND PROGRAM
PROGRAM COST SUMMARY**

Totals as of July 31, 2011

		Current Project Budget	Total Estimated Construction Costs	Obligations / Commitments to Date	Paid to Date	Open Encumbrance	% Obligated	% Complete
Project	Yuba College - Marysville (continued)							
J-28	Swing Space	\$ 1,031,146	\$ 915,158	\$ 931,640	\$ 927,140	\$ 4,500	90.35%	89.91%
J-47	YC Maintenance Equipment	\$ 279,270	\$ -	\$ 279,270	\$ 279,270	\$ -	100.00%	100.00%
J-48	Rad. Tech Relocation	\$ 305,547	\$ 227,618	\$ 28,993	\$ 28,993	\$ -	9.49%	9.49%
	Subtotal Yuba College - Marysville	\$ 86,758,740	\$ 63,544,829	\$ 52,300,575	\$ 41,399,859	\$ 11,045,109	60.28%	47.72%
Project	Yuba College - Clear Lake Campus							
J-31	Pay Off COPS	\$ 3,053,259	\$ -	\$ 3,053,259	\$ 3,053,259	\$ -	Complete	
J-32	Student Services Center	\$ 17,194,309	\$ 12,160,000	\$ 5,716,867	\$ 2,781,293	\$ 2,935,574	33.25%	16.18%
J-33	Renovate Portables & Upgrade Utilities	\$ 955,832	\$ 559,013	\$ 127,894	\$ 122,332	\$ 5,562	13.38%	12.80%
	Subtotal Yuba College - Clear Lake Campus	\$ 21,203,400	\$ 12,719,013	\$ 8,898,020	\$ 5,956,884	\$ 2,941,136	41.97%	28.09%
Project	Woodland Community College							
J-34	Performing Arts Center/ Culinary Arts	\$ 29,163,034	\$ 18,709,839	\$ 889,130	\$ 889,130	\$ -	3.05%	3.05%
J-35	Renovate Bldg 700	\$ 3,686,283	\$ 2,271,136	\$ 3,373,891	\$ 3,327,879	\$ 46,011	91.53%	90.28%
J-36	Multi-Purpose Facility	\$ 20,232,823	\$ 14,585,223	\$ 393,352	\$ 393,239	\$ 113	1.94%	1.94%
J-37	Soccer Field (Deferred)	\$ -	\$ -	\$ -	\$ -	\$ -	-	-
J-38	Baseball Field (Deferred)	\$ -	\$ -	\$ -	\$ -	\$ -	-	-
J-39	Multi Bldg Renovations	\$ 3,698,134	\$ 2,607,527	\$ 5,227,570	\$ 2,074,566	\$ 3,153,005	141.36%	56.10%
J-40	Grounds Improvements	\$ 1,154,729	\$ 628,374	\$ 1,024,431	\$ 1,024,431	\$ -	88.72%	88.72%
J-41	Softball Field (Deferred)	\$ -	\$ -	\$ -	\$ -	\$ -	-	-
J-42	Colusa County Out Reach Facility	\$ 6,503,616	\$ 3,346,630	\$ 5,698,719	\$ 5,001,019	\$ 697,700	87.62%	76.90%
J-46	WCC Maintenance Equipment	\$ 150,000	\$ -	\$ 151,850	\$ 128,255	\$ 30,699	101.23%	85.50%
	Subtotal Woodland Community College	\$ 64,588,619	\$ 42,148,729	\$ 16,758,943	\$ 12,838,519	\$ 3,927,528	25.95%	19.88%
Project	Equipment							
J-43	Group II Equipment	\$ 10,379,825	\$ -	\$ 123,428	\$ 119,228	\$ 4,200	1.19%	1.15%
TOTAL PROJECT COSTS		\$ 230,408,465	\$ 145,612,571	\$ 101,232,389	\$ 80,013,087	\$ 21,370,798	43.94%	34.73%

¹ Expenditures in projects J-44 & J-45 are distributed to all applicable projects at the end of each fiscal year.

Budget updates are in progress in conjunction with Fiscal Year end closeout to reflect Measure J Bond expenditure requirements.

**YUBA COMMUNITY COLLEGE DISTRICT
MEASURE J BOND PROGRAM
PROJECT STATUS MATRIX**

July 31, 2011

		Planning / Pre-Design	A/E Selection	Programming	Schematic Design	Design Development	Construction Documents	DSA	Bid & Award	Construction	Close-Out	Remarks
J-01	Sutter County Facility											Lease/Leaseback, GMP
J-01	Increment 1: Site Work									●		
J-01	Increment 2: Building								●			
J-02*	Bldg 100A – Administration Bldg				●							
J-03*	Bldg 100B – Student/Instruction Services				●							
J-04*	Bldg 200 – Music Department				●							
J-05*	Bldg 300 – Student Center/Bookstore						●					
J-06	Bldg 400 – Theatre										●	
J-07*	Bldg 500 – Business Dept (Classrooms)							●				
J-08	Bldg 600 – Applied Arts, Science/Tech											Project Complete.
J-09*	Bldg 700 – Math/Engineering/Computer							●				
J-10	Bldg 800 – Life Sciences & Nursing											Project Complete.
J-11	Bldg 900 – Utilities Services/Fire Water											Project Complete.
J-12	Bldg 1000 – Liberal Arts Consumer Ed											Project Complete.
J-12	Bldg 1000 – Roof Repair											Project Complete.
J-13	Bldg 1100 – Library & Language Arts								●			State Funded. Lease/Leaseback, GMP.
J-14	Bldg 1200 – Athletic Dept & Gym (Bldg.)									●		
J-14	PE Complex Athletic Fields										●	
J-15	Bldg 1250 – ESL (Demolish Structure)			●								
J-17	Bldg 1400 – Maintenance/Print Shop	●										
J-18	Bldg 1500 – Osuna (Demolish Structure)											
J-20	Bldg 1700 – Automotive			●								On hold pending relocation of J-48 Rad Tech
J-21	Bldg 1800 – Student Services Renovation											Project Complete.
J-21	Bldg 1800 – Student Services ADA Upgrades											Project Complete.
J-22	Bldg 1900 – Distributive Ed Center											Project Complete.
J-23	East Parking Lot – Resurface											Included in project J-25. Project complete.
J-24	New Soccer Field										●	Included in project J-14
J-25	Health & Public Safety Building											
J-25	Increment 1: Site Work, E. Parking, Campus Walk											Project Complete.
J-25	Increment 2: Building									●		
J-26	Upgrade Press Box/Score Board, Etc										●	Included in project J-14
J-27	Demolition Pool										●	Included in project J-14
J-28	Swing Space											Project Complete.

*Further progress pending District determination of available funding.

**YUBA COMMUNITY COLLEGE DISTRICT
MEASURE J BOND PROGRAM
PROJECT STATUS MATRIX**

July 31, 2011

		Planning / Pre-Design	A/E Selection	Programming	Schematic Design	Design Development	Construction Documents	DSA	Bid & Award	Construction	Close-Out	Remarks
J-30	Emergency Backup Generator											Project Complete.
J-30	Server Room HVAC Upgrade											Project Complete.
J-30	Server Room Wire Mgmt & Racks											Project Complete.
J-32	Student Services Center (Clear Lake Campus)											Lease/Leaseback, GMP.
J-01	Increment 1: Site Work									●		
J-01	Increment 2: Building							●				
J-33	Renovate Portables & Upgrade Utilities									●		
J-34	Performing Arts Center/Culinary Arts		●									Potential State Funding.
J-35	Renovate Bldg 700											Project Complete.
J-36	Multi-Purpose Facility											Potential State Funding.
J-37	Soccer Field											Deferred/potential State Funding.
J-38	Baseball Field											Deferred/potential State Funding.
J-39	Multi Bldg Renovations											
J-39	Increment 1. Bldg. 100/300/400 Re-Roof										●	
J-39	Increment 2: Bldg. 100/300/400 Renovation									●		
J-39	Bldg. 300 - Campus Police Relocation											Project Complete.
J-39	Bldg. 300 - Geology Lab Relocation											Project Complete.
J-40	Grounds Improvements											Project Complete.
J-40	Parking ADA Access											Project Complete.
J-40	Domestic Water Connection											Project Complete.
J-41	Softball Field											Deferred/potential State Funding.
J-42	Colusa County Outreach Facility										●	Completion of site work remains.
J-48	Bldg 1700 – Radiation Tech Relocation			●								



Measure J Bond Program Status Report
as of July 31, 2011
Attachment D



Landscaping Nearly Complete, Woodland CC
Colusa County Outreach Facility




Multi-Building Renovations in Progress
Woodland Community College



Temporary Computer Cyber Lab
Building 1100, Library/LRC Renovation, Yuba College



Temporary Quiet Study
Building 1100, Library/LRC Renovation, Yuba College

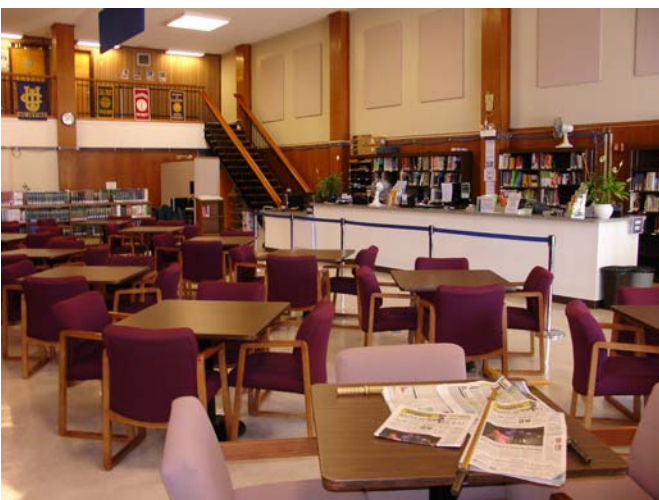

Temporary Library
Building 1100, Library/LRC Renovation, Yuba College



Renovated Coach Office
Building 1200, PE Complex Vol II., Yuba College
